



# DR-4344-CA

---

Mendocino County Board of Supervisors

Briefing

February 6, 2018

Jodi Traversaro  
Cal OES Branch 1 Director

Robert M. Pesapane  
FEMA Branch 1 Director



FEMA

# Mendocino County Debris Mission Update

## Cumulative Totals as of 2/4/18:

- Parcels Cleared of Debris: **245**
- Parcels released to County: **135**
- Tons of Debris Removed: **81,901**

## Call Center Volume:

- 2/4 - 0
- 2/3 - 5
- 2/2 - 0
- 2/1 - 1
- 1/31 - 1

## Average Daily Totals:

- Debris Removal Teams: **19**
- Debris Tons Removed: **2,407**


## Issue Resolution Status :

- 8 Tracked Issues
  - 7 Open Cases
  - 1 Closed
- Open cases are undergoing process and awaiting formal response, soil samples or final determination of case
- 6 of Quality Assurance Staff in the Field



US Army Corps  
of Engineers®

# Mendocino County Debris Removal Mission Look Ahead

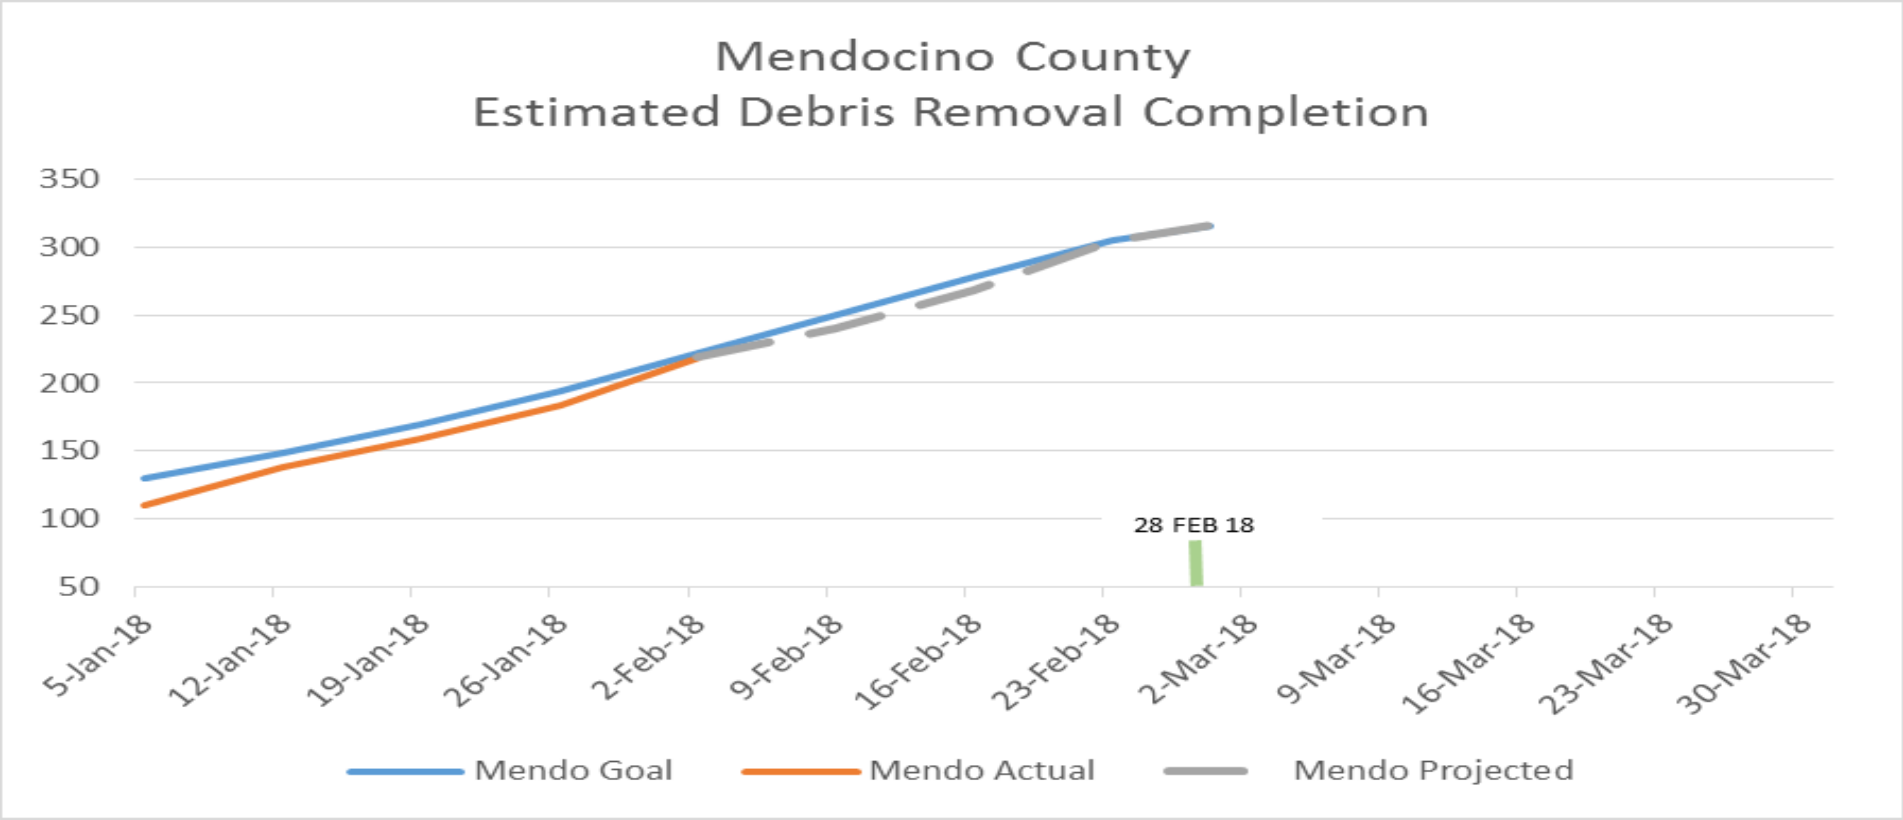


Estimated Completion Date : 28 FEB 18



**Cal OES**  
GOVERNOR'S OFFICE  
OF EMERGENCY SERVICES




FEMA



US Army Corps  
of Engineers®

## PHASE II PRIVATE PROPERTY DEBRIS REMOVAL PROCESS & TIMELINE

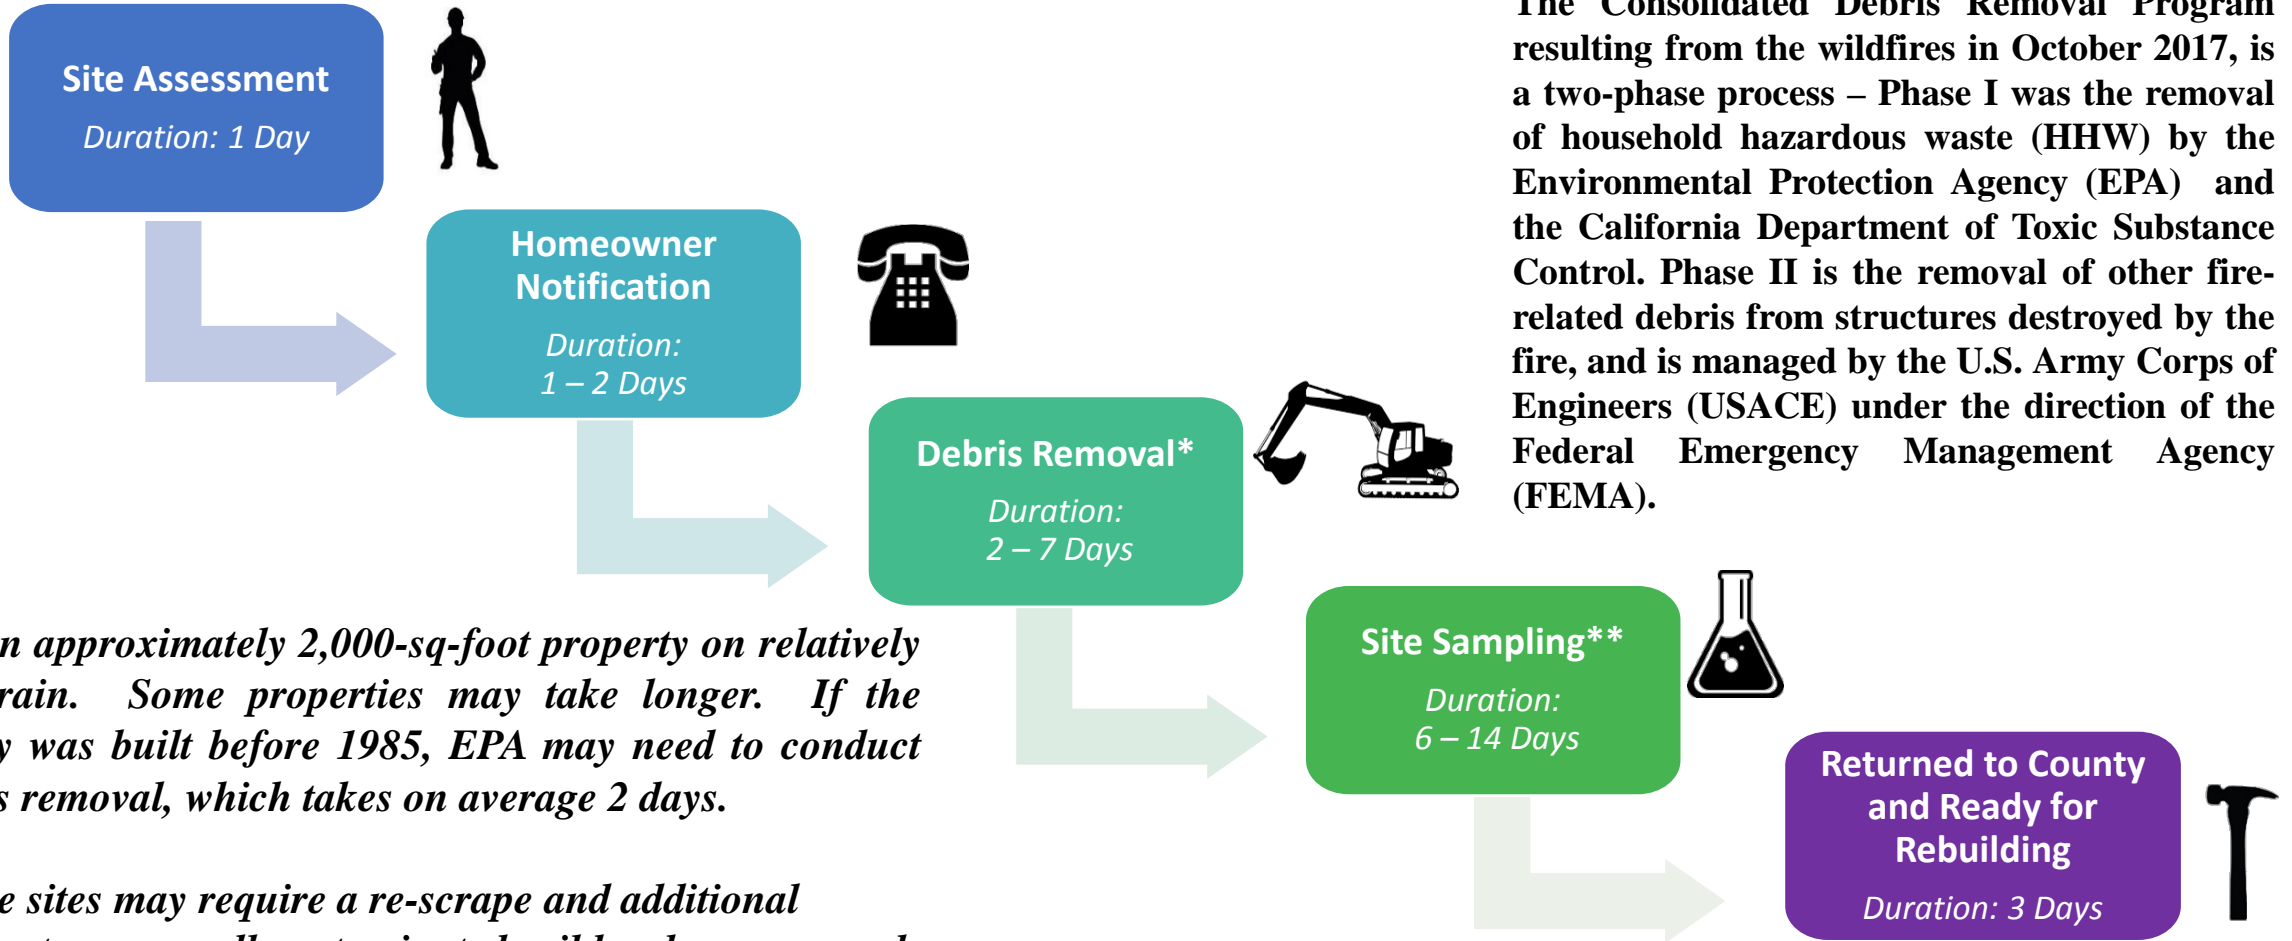

The Consolidated Debris Removal Program resulting from the wildfires in October 2017, is a two-phase process – Phase I was the removal of household hazardous waste (HHW) by the Environmental Protection Agency (EPA) and the California Department of Toxic Substance Control. Phase II is the removal of other fire-related debris from structures destroyed by the fire, and is managed by the U.S. Army Corps of Engineers (USACE) under the direction of the Federal Emergency Management Agency (FEMA).

*\* For an approximately 2,000-sq-foot property on relatively flat terrain. Some properties may take longer. If the property was built before 1985, EPA may need to conduct asbestos removal, which takes on average 2 days.*

*\*\* Some sites may require a re-scrape and additional sampling to ensure all contaminated soil has been removed.*



**Cal OES**  
GOVERNOR'S OFFICE  
OF EMERGENCY SERVICES



**FEMA**



US Army Corps  
of Engineers®

# Debris Removal

## Property Owner Issue Resolution Process

### *Still In Development*

#### Issue Resolution Form

Issues reported through  
Info Line or other means.  
Form outlines the who,  
what, when, where and  
how.

#### Data Collection

USACE team reviews Issue  
Resolution Form, Right of  
Entry, Site Assessment, and  
other relevant facts.

If needed, a site visit and  
interviews are conducted.

#### Technical Review and Analysis

USACE field staff determines  
whether issue was caused by  
normal debris clearance  
operations. Any damage will  
be evaluated on a case by  
case basis to determine if  
corrective action is warranted.

#### Response & Resolution

Property owners will  
be contacted by  
USACE regarding how  
their issue will be  
resolved.

For more information, questions or  
concerns contact:

Debris Removal Information Line:  
877.875.7681

Interactive Status Map:

[www.spk.usace.army.mil/CAwildfire](http://www.spk.usace.army.mil/CAwildfire)



**Cal OES**  
GOVERNOR'S OFFICE  
OF EMERGENCY SERVICES



FEMA

# Mendocino County FEMA Direct Housing Update

## Cumulative Totals as of 2/5/18:

- 36 families eligible for FEMA Direct Housing.
  - 27 families have been housed in FEMA units.
    - 21 families housed in RVs at Redwood Empire
    - 2 families housed in MHUs on Private Sites
    - 4 families housed in Apartments/Houses
  - 9 families remain to be housed.
    - 2 awaiting RV arrival at Redwood Empire
    - 2 awaiting apartments or commercial MHU site
    - 5 awaiting private site MHU placement

## **Kyen Campground**

- Received bids from contractor and in process of getting approval from HQ to move forward with project
- Once approved, construction should begin within 7 days and work should take 30 days
- Estimated completion date: Mid-March.



FEMA
